Draft Act 2 Environmental Schedule
Updated July 7, 2017
Former Melody Tent / Civic Arena
Pittsburgh, PA

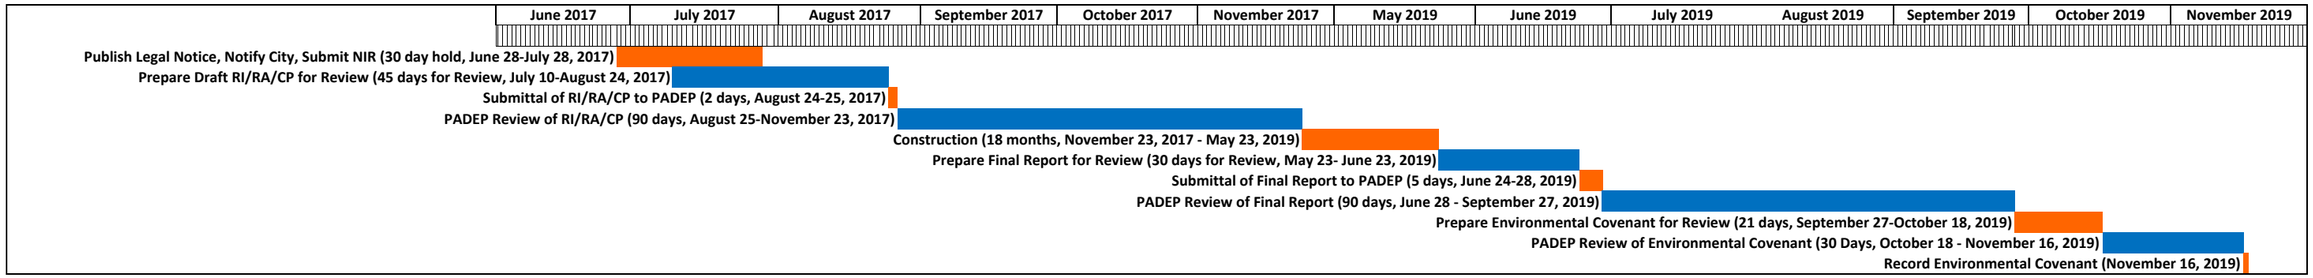

Milestone	Status
Collect 2nd Round Groundwater/Soil Gas (3 days, June 6-8, 2017)	Completed 6/8/17
Review of Notice of Intent to Remediate (10 days, June 6-16, 2017)	Completed 6/26/17
Publish Legal Notice, Notify City, Submit NIR (30 day hold, June 28-July 28, 2017)	Legal Notice-City Notification Completed 6/28/17 currently in 30 day hold
Prepare Draft RI/RA/CP for Review (45 days for Review, July 10,2017-August 24, 2017)	On Schedule
Submittal of RI/RA/CP to PADEP (2 days, August 24, 2017-August 25, 2017)	Pending
PADEP Review of RI/RA/CP (90 days, August 25 - November 23, 2017)	Pending
Construction (18 months, November 23, 2017 - May 23, 2019)	Pending
Prepare Final Report for Review (30 days for Review, May 23 - June 23, 2019)	Pending
Submittal of Final Report to PADEP (5 days, June 24-28, 2019)	Pending
PADEP Review of Final Report (90 days, June 28 - September 27, 2019)	Pending
Prepare Environmental Covenant for Review (21 days, September 27-October 18, 2019)	Pending
PADEP Review of Environmental Covenant (30 Days, October 18 - November 16, 2019)	Pending
Record Environmental Covenant (November 17, 2019)	Pending
